



96-inch Water Transmission Main Relocation

Project Updates

Content updated on 6/24/2025.



Phase 1 – Avon Road Construction Complete

Phase 1 – Avon Road Construction Complete

East Avon Road reopened to traffic on August 25, 2023


Construction photos of 96-inch welded steel pipe installation on Avon Road and Clinton River crossing:



Phase 1 – Avon Road Construction Complete

East Avon Road reopened to traffic on August 25, 2023

Phase 1 Avon Road reconstruction, widening, and new roundabout at 23 Mile Road and Dequindre Road:

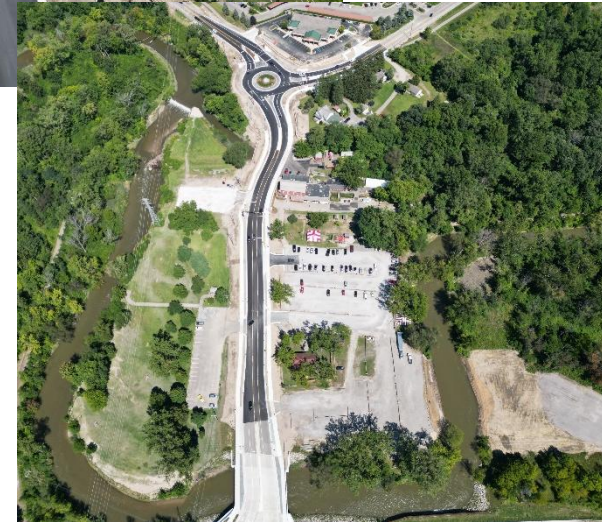


Phase 2 – Dequindre Road Construction Status Updates

Phase 2 – Construction Status Updates

Phase 2 Scope and Schedule:

- Construction of additional 8,000 feet of 96-inch water transmission main (WTM) in Dequindre Road
- Construction began in “South Dequindre” segment on November 6, 2023 (Detour 1)
- Paving in “South Dequindre” is complete and reopened to traffic on October 25, 2024
- North Dequindre Road Closure (Detour 2) scheduled from October 28, 2024 through July 2025
- **Paving in “North Dequindre” is anticipated to be complete and reopened to traffic in July 2025**
- Contract Final Completion of Phase 2: December 31, 2025

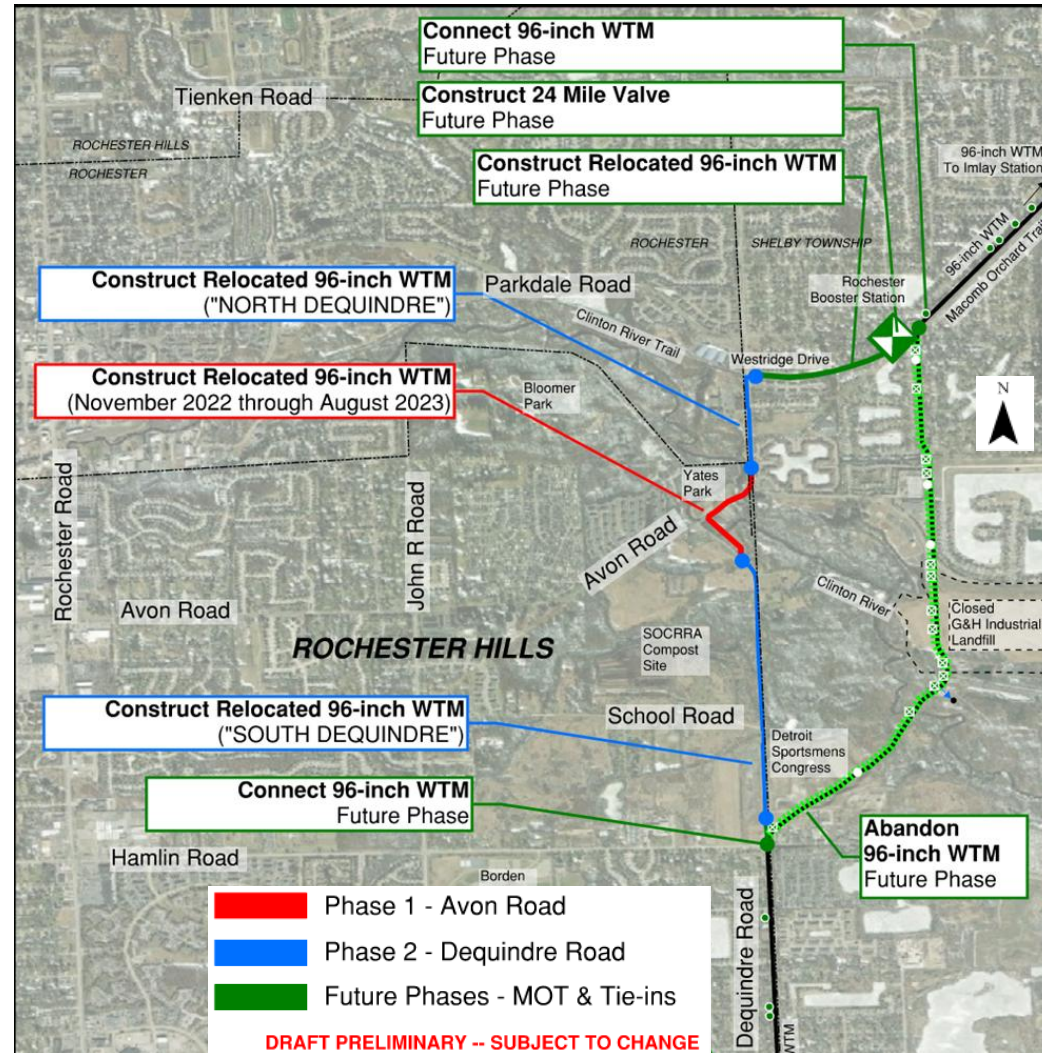

Phase 2 – Construction Status Updates

Phase 2 – Dequindre Road Detour 2 Map


- **Detour 2:**
October 28, 2024 through July 2025
- Detour 2 remains in place until completion of North Dequindre roadway pavement restoration (anticipated July 2025)



Phase 2 – Construction Status Updates

Phase 2 – Trail Detour Map

- **Trail Detour:**
November 2024 through July 2025
- Trail Detour remains in place until completion of North Dequindre roadway pavement restoration (anticipated July 2025)

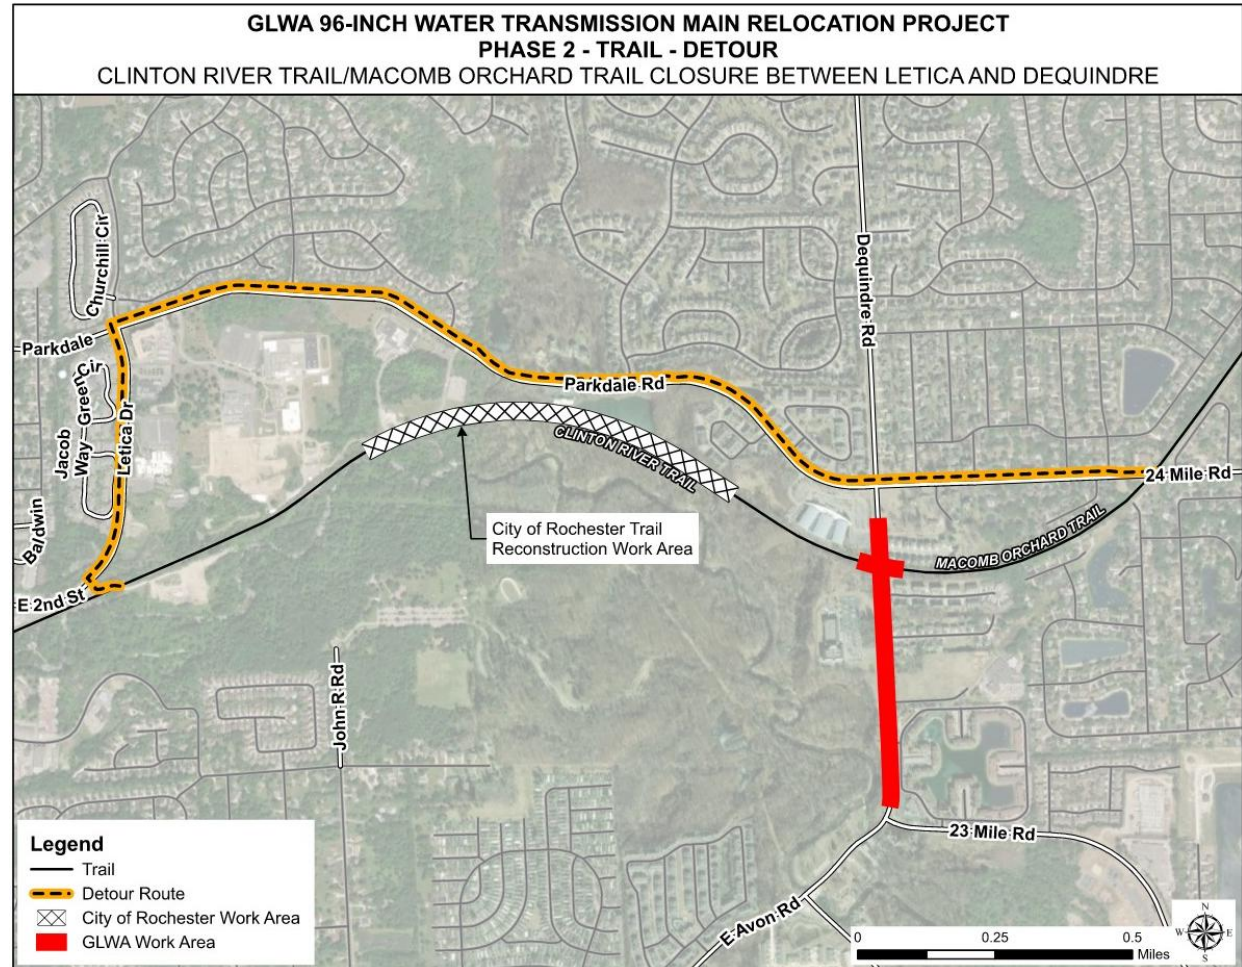

Phase 2 – Construction Status Updates

Post GLWA Construction Trail Detour Map

- Trail Detour along Clinton River Trail remains in place until completion of trail restoration by City of Rochester. Questions related to Clinton River Trail should be directed to City of Rochester.



Phase 2 – Construction Status Updates

- **South and North Dequindre:** About 8,000 feet of 96-inch welded steel pipe installed; pipe installation complete



Phase 2 – Construction Status Updates

- Final restoration is complete with aggregate base installation, road-side ditches, shoulder installation, and asphalt paving; North Dequindre restoration remains on schedule



Stakeholder Coordination Information

Project Web Page: www.glwater.org/96inchwatermain/

Web page will be updated as new information becomes available. Frequently Asked Questions will be revised as project progresses. A web form is available to register for email updates.

Project Email Address: 96inchwatermain@glwater.org

Project Hotline Voicemail Number: **1-877-237-7311**

Project Progress Updates: The GLWA Project Team coordinates consistently with key stakeholders and provides design progress updates at key design milestones.



GLWA

Great Lakes Water Authority
