



96-inch Water Transmission Main Relocation

Project Updates

Content updated on 10/25/2024.



Phase 1 – Avon Road Construction Complete

Phase 1 – Avon Road Construction Complete

East Avon Road Reopened to traffic on August 25, 2023

Construction photos of 96-inch welded steel pipe installation on Avon Road and Clinton River crossing:



Phase 1 – Avon Road Construction Complete

East Avon Road Reopened to traffic on August 25, 2023

Phase 1 Avon Road reconstruction, widening, and new roundabout at 23 Mile Road and Dequindre Road:




Phase 2 – Dequindre Road Construction Status Updates

Phase 2 – Construction Status Updates

Phase 2 Scope and Schedule:

- Construction of additional 8,000 feet of 96-inch water transmission main (WTM) in Dequindre Road
- Construction began in “South Dequindre” segment on November 6, 2023 (Detour 1)
- Paving in “South Dequindre” is complete and reopened to traffic on October 25, 2024
- North Dequindre Road Closure (Detour 2) scheduled from October 28, 2024 through Fall 2025
- Work in “South Dequindre” and “North Dequindre” segments will not occur concurrently
- Final Completion of Phase 2: December 31, 2025

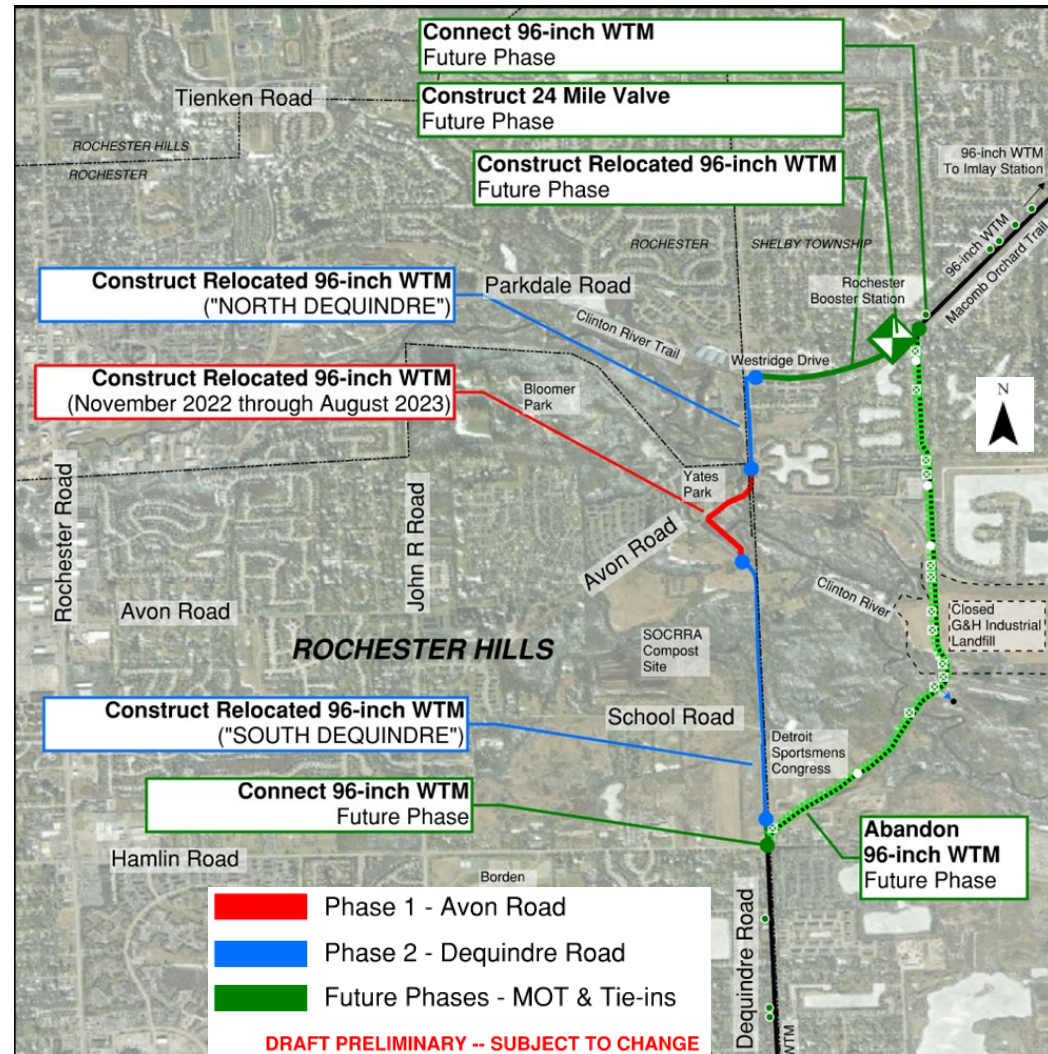

Phase 2 – Construction Status Updates

Phase 2 – Dequindre Road Detour 2 Map


- **Detour 2:**
October 28, 2024 through Fall 2025
- Detour 2 remains in place until completion of North Dequindre roadway pavement restoration



Phase 2 – Construction Status Updates

Phase 2 – Trail Detour Map

- **Trail Detour:**
November 2024 through
Fall 2025
- Trail Detour remains in
place until completion of
North Dequindre roadway
pavement restoration

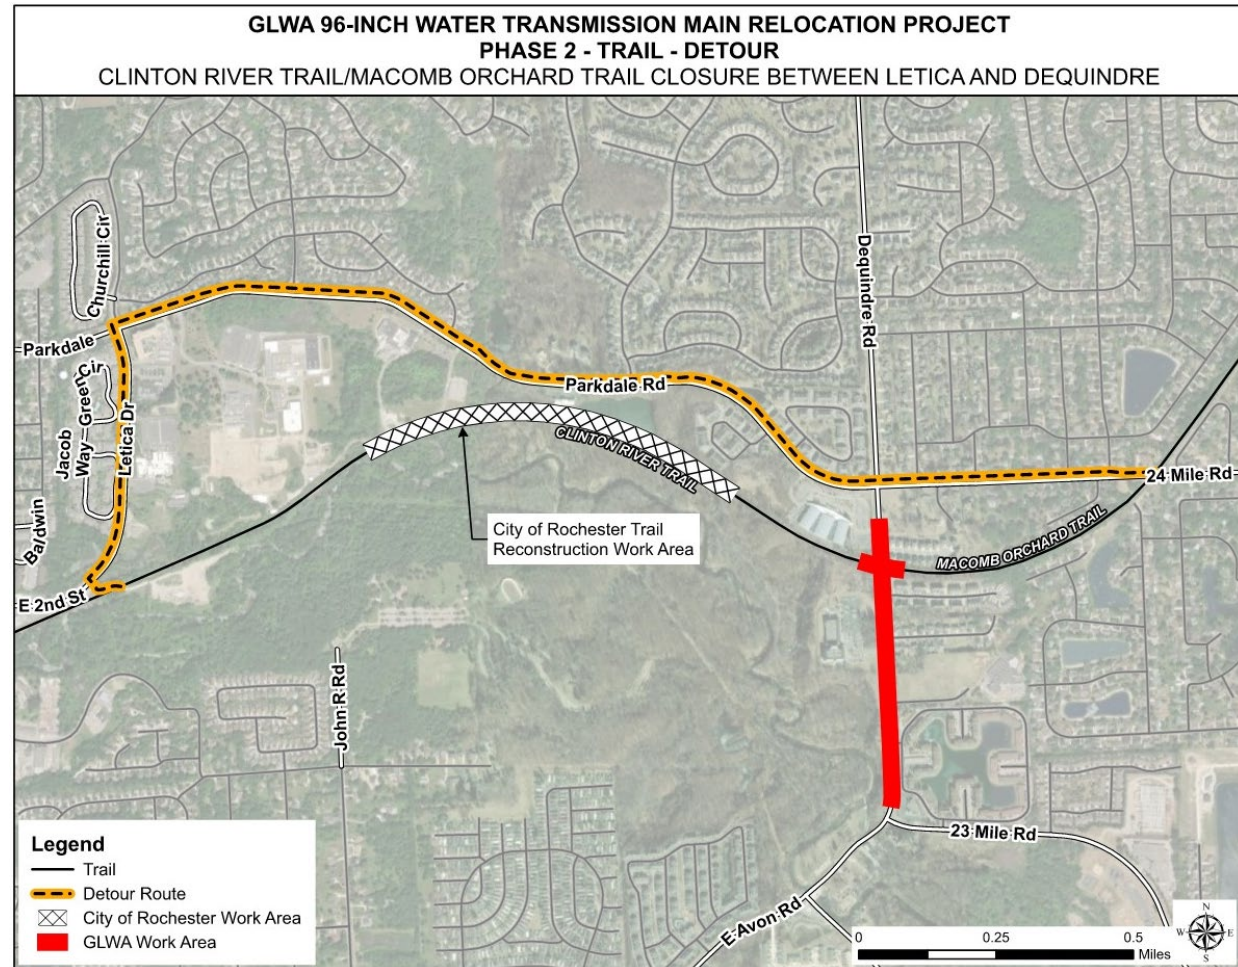

Phase 2 – Construction Status Updates

- **South Dequindre:** About 6,000 feet of 96-inch welded steel pipe installed; pipe installation remains on schedule



Phase 2 – Construction Status Updates

- **South Dequindre:** Final restoration has begun with aggregate base installation, road-side ditches, shoulder installation, and asphalt paving; restoration remains on schedule



Stakeholder Coordination Information

Project Web Page: www.glwater.org/96inchwatermain/

Web page will be updated as new information becomes available. Frequently Asked Questions will be revised as project progresses. A web form is available to register for email updates.

Project Email Address: 96inchwatermain@glwater.org

Project Hotline Voicemail Number: **1-877-237-7311**

Project Progress Updates: The GLWA Project Team coordinates consistently with key stakeholders and provides design progress updates at key design milestones.



GLWA

Great Lakes Water Authority
